ENTERPRISE TRANSFORMATION PROPOSAL

Titagarh AI Transformation & Value Realisation Partnership

A twelve-month partnership to convert AI capability into measurable improvement across project execution, material availability, bid-to-delivery continuity and management decision-making.

PREPARED FOR	PREPARED BY
Titagarh Rail Systems Limited	**Altrd**
DOCUMENT STATUS	**DATE**
Working draft for discussion	August 2026

PROPOSED ENTERPRISE MANDATE

Establish a governed transformation programme that continuously identifies, redesigns, implements and scales priority workflows across Titagarh.

DOCUMENT GUIDE

Contents

The proposal moves from evidence of readiness to the enterprise operating model, value portfolio, partnership scope and commercial architecture.

FOUNDATION & PROGRAMME			PORTFOLIO, PARTNERSHIP & MOBILISATION		
NO.	SECTION	PAGE	NO.	SECTION	PAGE
01	Executive recommendation	03	10	Illustrative value cases	12
02	Closing Phase 1	04	11	Illustrative value cases	13
03	The AI-native model	05	12	Governance and value	14
04	The next enterprise mandate	06	13	Transformation roadmap	15
05	How the programme works	07	14	Dedicated enterprise pod	16
06	First eight weeks	08	15	Partnership scope	17
07	Data foundation	09	16	Commercial architecture	18
08	Product delivery	10	17	Mobilisation	19
09	Initial enterprise portfolio	11			

DECISION SEQUENCE **Read the headlines as one executive argument**

Titagarh has built readiness. The partnership converts that readiness into a governed portfolio, value-backed products and sustained operating improvement.

01 | EXECUTIVE RECOMMENDATION

Titagarh has created AI readiness. The next mandate is to convert it into enterprise value.

The two-day company-wide Claude bootcamp has established a shared understanding of AI, hands-on experience across departments and an initial pipeline of opportunities.

RECOMMENDATION **Appoint Altrd to establish and run Titagarh's AI Transformation & Value Realisation Office**

The twelve-month mandate will create one governed portfolio across departments, redesign priority workflows, enable the data they require, commission value-backed products and track benefits through adoption.

What has been achieved	What the next mandate unlocks
Company-wide AI fluency	Enterprise priorities replace disconnected department ideas.
Hands-on Claude experience across departments	Workflow redesign moves AI into repeatable operating processes.
Early use cases surfacing through real work	The strongest opportunities move through a disciplined value and investment gate.

STRATEGIC SHIFT **From individual productivity to repeatable operating advantage**

The opportunity now extends beyond helping people complete existing tasks faster. It is to change how priority work is designed, governed and scaled.

02 | CLOSING PHASE 1 (YET TO BE DONE. TAKE THIS AS STEP 1)

Consolidate adoption while opening the enterprise opportunity funnel

One 45-minute online recap per department confirms access, resolves practical questions and captures one or two opportunities grounded in real work.

0-10 minutes	10-20 minutes	20-45 minutes
Access and refresh	Open floor for practical doubts	Identify one or two use cases
Confirm seats, logins and safe-use principles.	Discuss where Claude helped, failed or created uncertainty.	Capture the problem, owner, frequency, inputs and desired outcome.

Why this bridge matters

Post-training reality	Programme response
Access can lapse	Permission and login issues are closed before enterprise work begins.
Questions become more specific	Safe-use guidance is anchored in actual department tasks.
Use cases become sharper	The strongest ideas enter a governed opportunity portfolio.

PHASE 1 EXIT CONDITION

Every participating department has a named owner and documented opportunity set


The recap protects the value of the bootcamp while supplying evidence for the first redesign wave.

03 | THE AI-NATIVE MODEL

Four capabilities convert AI potential into operating advantage

People create adoption. Data creates access. Workflow redesign changes how work runs.

Systems make the new way of working repeatable at scale.



PROGRAMME LOGIC **The four capabilities must advance as one portfolio**

Training without workflow change limits value. Systems without trusted data do not scale. Products without process ownership do not sustain adoption.

04 | THE NEXT ENTERPRISE MANDATE

Create a repeatable engine for AI-led transformation

The proposed partnership establishes a standing capability to identify value pools, redesign work, commission products and track benefits across the enterprise.


Mandate	What changes for Titagarh
One enterprise portfolio	Department ideas compete transparently for attention and investment.
A redesign-before-build discipline	Technology follows the future-state workflow, not the other way around.
Use-case-led data enablement	Connectors are created where a priority workflow proves the need.
Value-gated product delivery	Build decisions require a named owner, baseline, target and acceptance criteria.
Capability transfer by design	Titagarh teams learn the methods while real workflows and products are delivered.

TWELVE-MONTH OUTCOME **A governed portfolio of redesigned workflows and scalable AI products**
Success is measured through operating improvements that are adopted, evidenced and sustained.

05 | HOW THE PROGRAMME WORKS

Run transformation as an enterprise portfolio, not a collection of pilots

A single governance rhythm connects department demand, workflow redesign, data enablement, product investment and realised value.

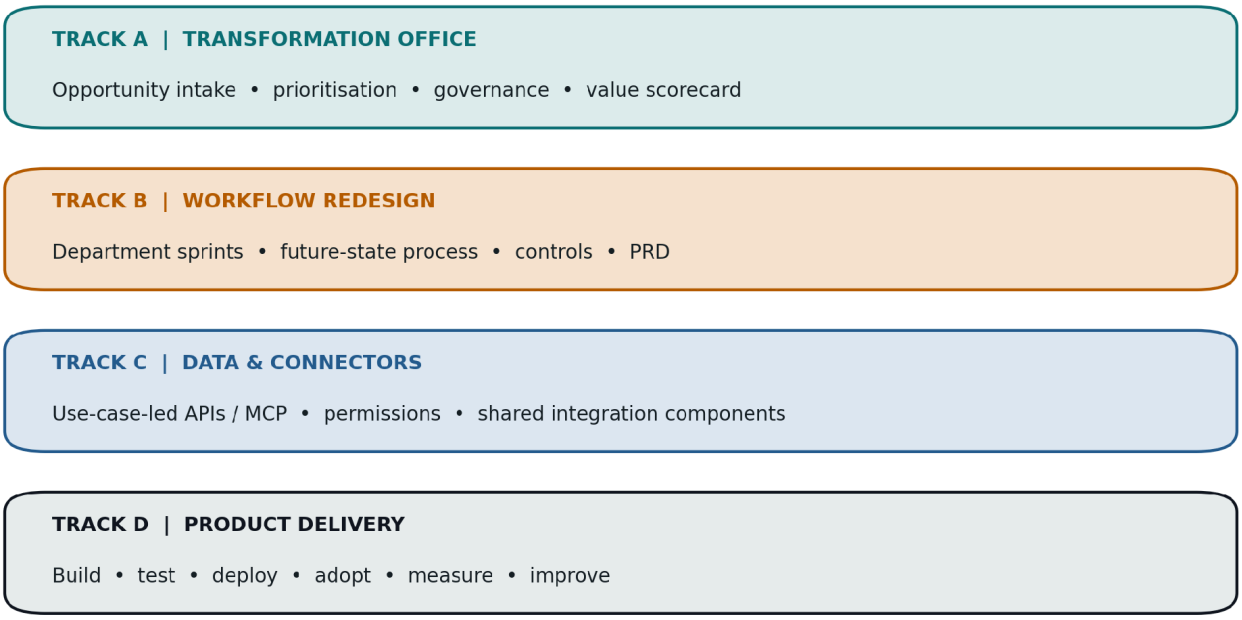


Decision	Accountable owner	Evidence required
Which workflow enters redesign?	Product & Value Council	Material problem, business owner and plausible value pool
Which product receives investment?	Executive Steering Committee	Future-state workflow, PRD, data plan, controls and value case
Which product scales?	Business outcome owner	Adoption, reliability and measured benefit after launch

06 | FIRST EIGHT WEEKS

Six departments enter a focused redesign and investment cycle

Three departments participate in each four-week wave. Each department advances one anchor workflow through three working sessions and an investment gate.

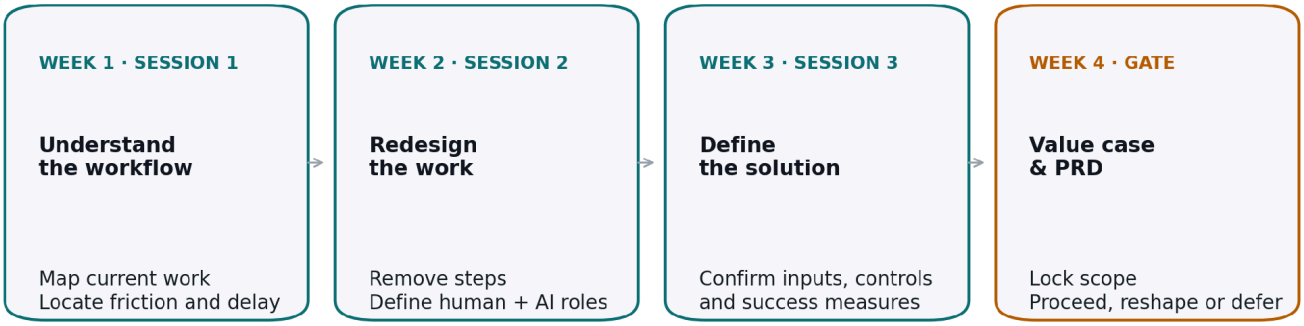

MONTH 1 3 departments in parallel | 1 structured meeting per department per week

MONTH 2 Next 3 departments enter redesign while approved product and connector work begins

OUTCOME: six redesigned workflows, a prioritised investment portfolio and implementation-ready PRDs for selected opportunities

Wave 1 | Month 1	Wave 2 | Month 2
Project Management Materials Management Bidding & Tendering	Shipbuilding Finance Human Resources


EIGHT-WEEK DELIVERABLE **Six redesigned workflows and a prioritised investment portfolio**

Selected opportunities proceed with implementation-ready PRDs. Others are sequenced, deferred or retired with a clear rationale.

07 | DATA FOUNDATION

Build a reusable decision layer, one priority workflow at a time

SAP, Ariba, Primavera, ZingHR and other systems are connected incrementally through governed APIs and MCP-compatible services.

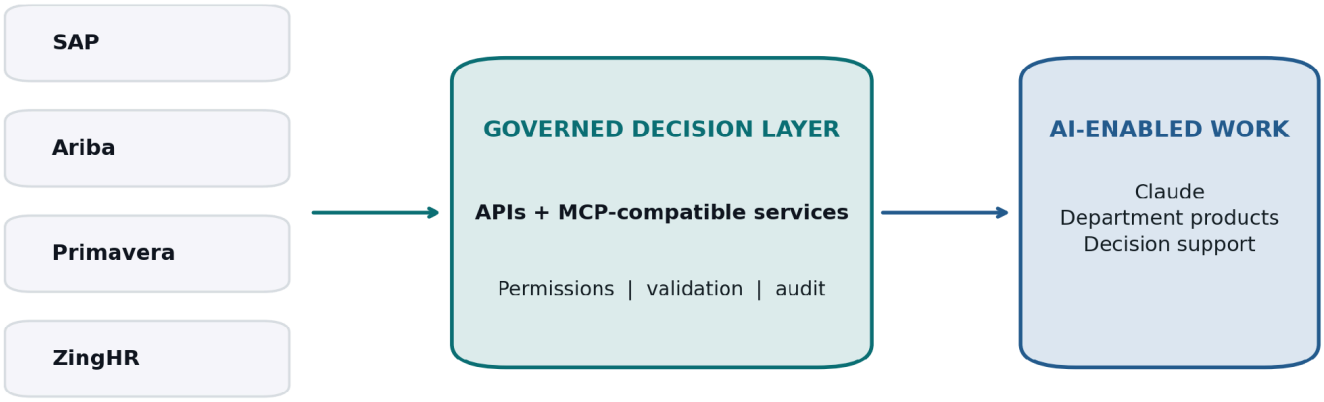

Each approved workflow adds reusable governed components to the enterprise foundation.

Today	Target state
Teams pull and reconcile information across systems.	Priority workflows retrieve governed information at the point of decision.
Each new tool risks repeating the same integration work.	Approved connectors become reusable enterprise components.


ARCHITECTURE PRINCIPLE **Build only what the portfolio needs, then reuse it**

Each approved product adds governed components to a shared enterprise foundation. This avoids a large front-loaded integration programme.

08 | PRODUCT DELIVERY

Every build begins with a clear workflow and value case

The portfolio creates the product pipeline. Each implementation then moves through a formal investment gate and a defined delivery lifecycle.

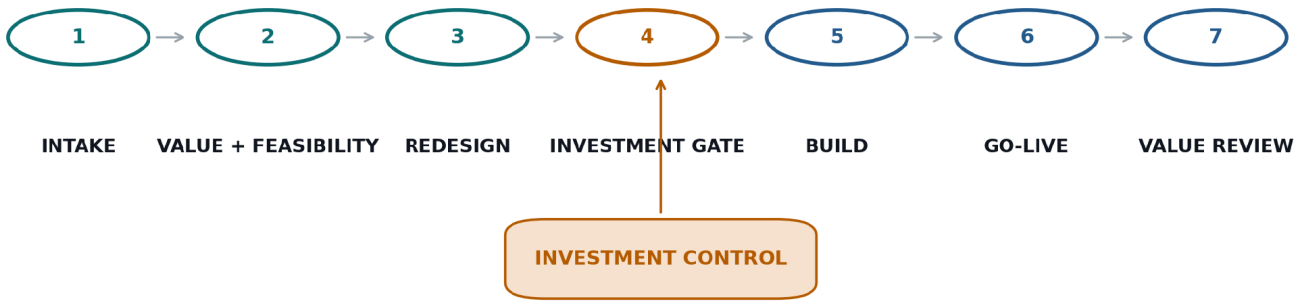

Investment pack	What must be explicit
Outcome and ownership	Baseline, target, measurement method and accountable business owner
Future-state workflow	Users, decisions, human approvals, exceptions and fallback
Product and data scope	Features, integrations, permissions, controls and exclusions
Delivery commitment	Milestones, testing, acceptance criteria and adoption plan

INVESTMENT DISCIPLINE **Proceed, reshape, defer or retire**

The programme protects capital by making the decision explicit before engineering begins.

09 | INITIAL ENTERPRISE PORTFOLIO

Begin with six value pools that matter to execution

These are starting hypotheses. The sprint validates the problem, owner, value, data and feasibility before any product receives investment.

Department	Anchor workflow to validate	Value lens
Project Management	Project status to early delay intervention	Predictability
Materials Management	Purchase requirement to material-risk action	Availability and working capital
Bidding & Tendering	Tender intake to risk review and project handover	Speed and risk
Shipbuilding	Vendor and production data to operating control	Execution control
Finance	Project commitments and actuals to budget intervention	Cost control
Human Resources	Candidate intake to compliant onboarding	Cycle time and completeness

PORTFOLIO RULE **Narrow enough to build. Important enough to matter.**
Each department advances one anchor workflow. The remaining ideas stay visible and compete for later capacity.

Three examples show how workflow redesign translates into measurable value

The product is defined only after the problem and future-state workflow are validated. Measures below are illustrative; baselines and targets are established in the sprint.

Project Management | Earlier visibility into delay risk

Problem	AI-enabled workflow	Measure
Updates are assembled manually across calls, messages and Primavera.	Controlled status intake highlights exceptions and critical-path changes for review.	Update latency; effort; risks identified before milestone impact

Materials Management | Earlier visibility into vendor risk

Problem	AI-enabled workflow	Measure
Material and vendor risks appear after they begin affecting schedules.	Requirements, purchase status, commitments and milestones are reviewed together.	PR-to-PO time; risk lead time; exception closure

Bidding & Tendering | Faster, more reliable qualification

Problem	AI-enabled workflow	Measure
Eligibility and contractual risks require repeated manual cross-checks.	Documents are structured once; exceptions and obligations move through defined approval.	Review cycle; missed clauses; handover completeness

Three further examples extend the portfolio across operations and corporate functions

Each concept follows the same logic: clarify the operating problem, redesign the work, then build and measure only what the future state requires.

Shipbuilding | Integrated vendor and operating control

Problem	AI-enabled workflow	Measure
Vendor status, payment stage and reliability are maintained in separate views.	A governed view connects performance, commitments and exceptions for action.	Reconciliation effort; disputes; exception resolution

Finance | Earlier visibility into project budget risk

Problem	AI-enabled workflow	Measure
Budget tracking is fragmented and overrun risk surfaces late.	Commitments and actuals are reviewed against budget with exception-led intervention.	Reporting latency; forecast accuracy; early warnings

Human Resources | Complete, faster onboarding

Problem	AI-enabled workflow	Measure
Documents and checklists are tracked manually and inconsistently.	A controlled onboarding workspace identifies missing items and routes follow-up.	Turnaround time; day-one completeness; manual follow-up

12 | GOVERNANCE AND VALUE

Tie every investment decision to a business owner and proof standard

Titagarh owns strategic priorities and business outcomes. Altrd provides portfolio leadership, delivery discipline, capability transfer and transparent value reporting.

Forum	Cadence	Decisions
Executive Steering Committee	Monthly	Priorities, investment gates, material risks and value actions
Product & Value Council	Fortnightly	Workflow selection, baselines, PRDs, releases and benefits
Delivery Working Group	Weekly	Requirements, dependencies, tests, issues and commitments
Adoption Office Hours	Monthly	Claude guidance, safe-use support and repeatable team solutions

One value ledger for every initiative

Baseline	Target	Owner	Proof	Decision
Current performance	Expected change	Named executive	Agreed evidence	Scale, improve or stop


VALUE DISCIPLINE **Separate forecast, validated and realised value**

Every benefit follows an agreed baseline, owner and proof standard. Executive reporting includes only evidence that meets the defined standard.

13 | TRANSFORMATION ROADMAP

The first eight weeks establish momentum; the next ten months compound value

Workflow redesign continues while selected products are built, adopted, measured and scaled. Sequencing follows value, readiness and dependency.

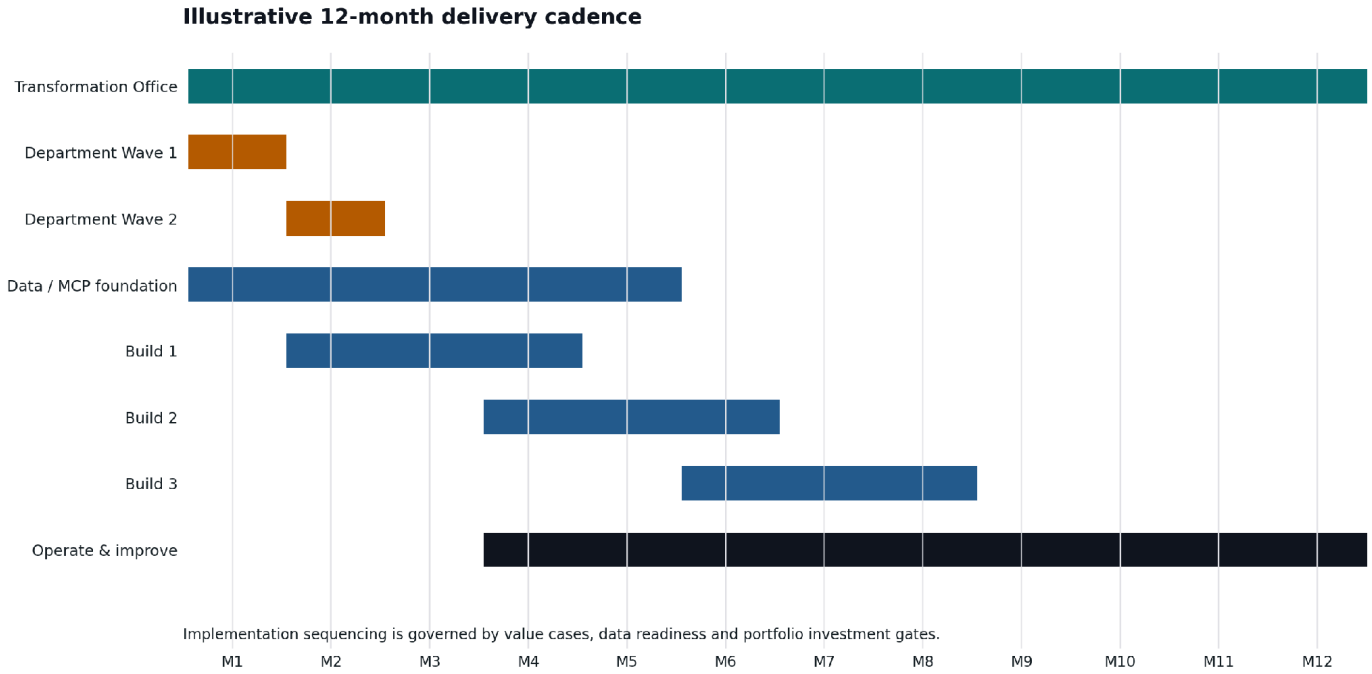

0-2 months	3-6 months	7-12 months
Mobilise governance Redesign six workflows Approve first value cases	Build lighthouse products Expand connector layer Measure adoption and value	Scale proven products Extend to new workflows Shape year-two portfolio

CAPABILITY TRANSFER **Build with the team. Document for the team. Transfer to the team.**
Working methods, PRDs, architecture, data definitions, runbooks, training and value scorecards are retained by Titagarh throughout delivery.

14 | DEDICATED ENTERPRISE POD

One accountable team carries the mandate from strategy through realised value

The annual partnership reserves a cross-functional Altrd leadership pod for Titagarh. Specialist engineering capacity is mobilised against approved product work orders.

Programme role	Engagement accountability
Executive sponsor	Senior relationship ownership, strategic escalation and quarterly value review
Transformation director	Programme leadership, stakeholder alignment and portfolio momentum
Portfolio and product lead	Opportunity qualification, workflow redesign, value cases and PRDs
AI and data architect	Architecture, data planning, connector strategy, controls and feasibility
Adoption and value lead	Claude support, capability transfer, adoption measurement and benefits tracking
Product engineering pod	Engineering, integration, QA and deployment for approved product work orders

Altrd is accountable across the full transformation journey

Strategise	Redesign	Architect	Build	Enable	Operate
Portfolio	Workflow	Data and controls	Approved products	Teams and owners	Live systems

WHY THIS MODEL WORKS **Continuity without creating dependency**

One team retains context from training through delivery, while methods, documentation and operating knowledge are transferred continuously to Titagarh.

15 | PARTNERSHIP SCOPE

Reserve continuous transformation capacity for Titagarh

The annual mandate provides the leadership, methods and delivery capacity required to sustain an enterprise portfolio. Product engineering and live operations remain separately commissioned.


Included in the annual mandate	Capacity and cadence
AI Transformation & Value Realisation Office	Twelve-month portfolio leadership and executive reporting
Department workflow redesign	Up to three active workstreams at a time
PRDs and value cases	Up to 12 implementation-ready packs per contract year, subject to complexity
Data and architecture planning	Use-case blueprints and connector plans
Capability transfer and Claude support	Executive briefings, owner training, technical pairing and office hours
Value realisation	Monthly scorecard and quarterly executive review

SCOPE BOUNDARY **Engineering and operations are commissioned separately**
This preserves transparency, gives Titagarh an investment gate for every product and prevents the annual mandate from becoming an undefined development retainer.

16 | COMMERCIAL ARCHITECTURE

Separate transformation capacity, product investment and live operations

The model creates predictable senior capacity while retaining scope and investment control at every product gate.

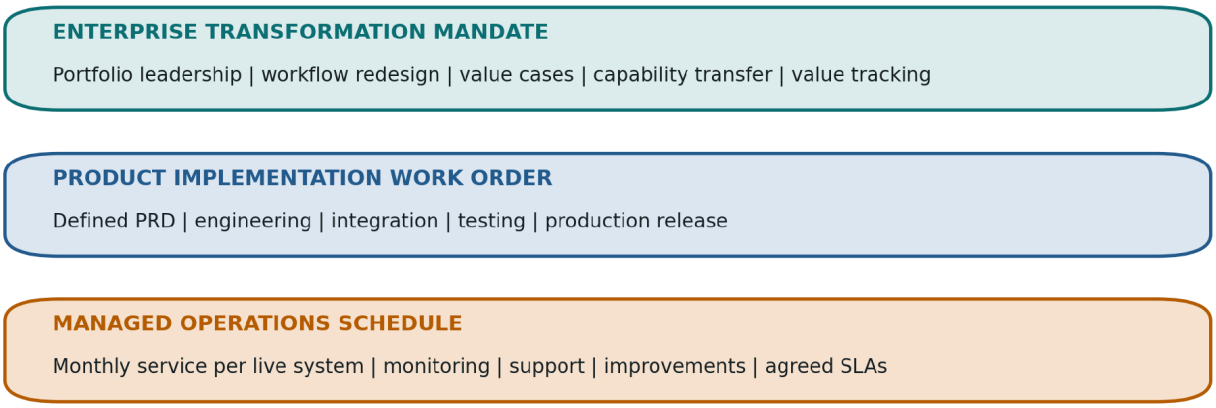

Commercial component	Pricing basis	Billing
Annual partnership	Fixed fee for agreed capacity	Quarterly in advance
Product implementation	Fixed fee against approved PRD	Milestone-based
Operate & maintain	Monthly fee by product and SLA	Monthly in advance
Infrastructure and licences	Cloud, APIs and third-party usage	Direct / monthly actuals

COMMERCIAL PRINCIPLE **Value before volume**

The annual mandate reserves transformation capacity. Every product is separately commissioned against a defined value case, scope, acceptance criteria and operating economics.

17 | MOBILISATION

The first 30 days establish control and activate the first portfolio wave

Mobilisation begins once the mandate, sponsorship, owners and working cadence are confirmed.

Week	Commitment	Decision or output
1	Confirm sponsor, programme owner, governance and working environment	Programme charter and decision calendar
1-2	Run 45-minute department recaps and consolidate opportunities	Access closed; doubts resolved; one or two use cases captured per department
2	Score opportunities and establish initial baselines	Wave 1 anchor workflows confirmed
3-4	Begin redesign with the first three departments	Future-state workflows and initial value cases in progress

Mobilisation enablers

Titagarh commitment	Why it matters
Executive sponsor and programme owner	Creates a clear decision and escalation path.
One contact and initial feedback per department	Allows recap sessions to begin with a real adoption picture.
Access pathway for in-scope systems and documents	Enables timely data and architecture assessment.
Consolidated use cases and agreed start date	Accelerates portfolio qualification and Wave 1 activation.

DAY-30 POSITION **A governed transformation portfolio is operating**
Titagarh has named owners, a prioritised opportunity set, initial baselines and three workflows actively being redesigned.

From AI awareness to repeatable operating advantage.
